



Middle Aston Limited

Hatch End Industrial Estate, Middle Aston

Construction Traffic Management Plan

December 2022



Middle Aston Limited

Hatch End Industrial Estate, Middle Aston

Construction Traffic Management Plan

OFFICE ADDRESS:

Butler House,
177 – 178 Tottenham Court Road,
London,
W1T 7NY

PROJECT NO:

J327040

DATE:

December 2022

REPORT No:	FILE NAME	PREPARED:	DATE OF ISSUE:	STATUS:	CHECKED:	AUTHORISED:
V1.0	221202 327040 CTMP V1.0.docx	KM	02 December 2022	Final	CH	CH

CHANGE LOG

VERSION	DATE:	CHECKED BY:	REASON FOR CHANGE:
V1.0	02 December 2022	CH	Initial Issue

CONTENTS

1	Introduction	4
1.	Overview	4
2.	Scope of Construction Traffic Management Plan	4
1.2	Development Proposal	5
1.3	Main Point of Contact	5
1.4	Structure of Report	5
2.	Policy and Guidance Context	7
2.1	OCC Local Transport Plan	7
2.2	Good Practice Guidance and Local Policy	7
3.	Existing Context	9
3.1	Site Location	9
3.2	Local Highway Network	10
3.3	Sustainable Travel Opportunities	10
4.	Construction Activity	12
4.1	Overview	12
4.2	Access to the Site	12
4.3	Site Staff	12
4.4	Schedule of Works	12
4.5	Construction Activity Time Periods	13
4.6	Delivery / Collection Management	13
4.7	Construction Staff Car Parking	13
4.8	Trip Generation	14
5.	Construction Traffic Management	15
5.1	Overview	15
5.2	Vehicle Activity and Routing	15
6.	Mitigation Measures	17
6.1	Overview	17
6.2	General Servicing Best Practice	17
6.3	Materials Storage and Security	17
6.4	Local Community Liaison	17
6.5	Noise and Vibration Management	18
6.6	Vehicle Checks	18
7.	Monitoring and Review	19

© Copyright mode transport planning. All rights reserved

This report has been prepared for the exclusive use of the commissioning party and unless otherwise agreed in writing with mode transport planning, no other party may copy, reproduce, distribute, make use of, or rely on the contents of the report. No liability is accepted by mode transport planning for any use of this report, other than for the purposes for which it was originally prepared and provided.

Opinions and information provided in this report are on the basis of mode transport planning using due skill, care and diligence in the preparation of the same and no explicit warranty is provided as to their accuracy. It should be noted and is expressly stated that no independent verification of any of the documents or information supplied to mode transport planning has been made.

8. Summary

20

8.1 Overview

20

APPENDICES

APPENDIX A Proposed Site Layout

1 Introduction

1. Overview

- 1.1.1 This Construction Traffic Management Plan (CTMP) has been prepared by mode transport planning (mode) on behalf of Middle Aston Limited to accompany a planning application for the redevelopment of the Hatch End Industrial Estate in Middle Aston, Oxfordshire.
- 1.1.1 The development proposals are for the erection of three new storage, warehousing and office units plus the expansion of one of the units (former Scout Hut, now known as unit 3) within the existing Hatch End Industrial Estate. The existing estate currently covers 2,246 square metres (sqm) (GIA) of commercial floorspace and with the addition of the proposed new commercial floorspace the entire estate will provide 14 business units comprising Class E(g) and B8 totalling 2,857sqm (GIA).
- 1.1.2 The development proposals include the provision of 24 new car parking spaces and 10 new cycle parking spaces and access arrangements retained onto Fir Lane. The net increase in commercial floorspace at the site is 611sqm. The proposed site layout is provided in [Appendix A](#).

2. Scope of Construction Traffic Management Plan

- 1.1.3 The aim of this CTMP is to outline the strategy for the safe and efficient movement of construction traffic associated with the construction activity at the redevelopment of the Hatch End Industrial Estate.
- 1.1.4 The strategy aims to minimise the impacts of construction traffic on the local highway network as well as minimise any environmental impacts as a result of the construction works taking place. In addition, care and due attention are given to the rural location of the site in relation to neighbouring properties.
- 1.1.5 The principal issues addressed within this CTMP are as follows:
- Schedule of works;
 - Deliveries and hours of operations;
 - Routing of construction traffic and delivery vehicles; and
 - Mitigation measures.
- 1.1.6 This CTMP explores the methods to keep construction vehicle activity to an efficient and manageable number of journeys to and from the site. This allows the timing of construction vehicle movements to avoid sensitive network (and school) periods, reducing noise and intrusion on the local area.

- 1.1.7 The CTMP is informed by local policy and guidance from Oxfordshire County Council (OCC) and the Department of Transport (DfT), as detailed in [Section 2](#).
- 1.1.8 This CTMP remains a draft at this planning application stage, ahead of planned construction activity being better understood, closer to construction inception.

1.2 Development Proposal

- 1.2.1 The development proposal are for the erection of three new storage, warehousing and office units plus the expansion of one of the units (former Scout Hut, now known as unit 3) within the existing Hatch End Industrial Estate. The existing estate currently covers 2,246sqm (GIA) of commercial floorspace and with the addition of the proposed new commercial floorspace the entire estate will provide 14 business units comprising Class E(g) and B8 totalling 2,857sqm (GIA).
- 1.2.2 The development proposals include the provision of 24 new car parking spaces and 10 new cycle parking spaces and access arrangements retained onto Fir Lane. The net increase in commercial floorspace at the site is 611sqm.

1.3 Main Point of Contact

- 1.3.1 The main point of contact in relation to the content of this CTMP during construction will be Mike Hawkins of Hawkins Group, available on 07989352245.

1.4 Structure of Report

- 1.4.1 The remaining sections of this CTMP are as follows:

[Section 2: Policy and Guidance Context](#)

- 1.4.2 This section details local policy and guidance applicable to this CTMP.

[Section 3: Existing Context](#)

- 1.4.3 This section details the site location, local highway network and sustainable travel options.

[Section 4: Construction Activity](#)

- 1.4.4 This section details the core construction activities and arrangements to be implemented by the Main Contractor including details on the site access, an indicative schedule of works, to efficiently manage and minimise the impact of construction.

[Section 5: HGV Management](#)

- 1.4.5 This section presents a traffic management plan which identifies appropriate access route(s) to and from the site. These routes seek to manage the impact of construction traffic on the local highway network.

Section 6: Mitigation Measures

- 1.4.6 This section details possible mitigation measures the Main Contractor can implement during the construction programme to manage the potential impact of construction traffic.

Section 7: Monitoring and Review

- 1.4.7 This section sets out a monitoring and review strategy.

Section 8: Summary

- 1.4.8 This section provides a summary of the CTMP.

2. Policy and Guidance Context

2.1 OCC Local Transport Plan

- 2.1.1 OCC Local Transport and Connectivity Plan (LTCP), was adopted in July 2022 and has been developed to ensure the County's transport systems support housing and economic growth, the transition to a low carbon economy and protect and enhance Oxfordshire's environment.
- 2.1.2 OCC's Freight and Logistics Strategy was also adopted in July 2022 and expands on the high-level policies within the LTCP regarding freight movement. The strategy states that major developments require the preparation of a Construction Logistics Plan (CLP) in order to *"reduce the impact construction has on local communities in relation to congestion, pollution and noise"*.
- 2.1.3 Full CLPs require:

"...detail such as the amount of construction traffic generation, the routes the construction vehicles will use and any traffic management that will be in place"

2.2 Good Practice Guidance and Local Policy

- 2.2.1 The Department for Transport (DfT) produced the 'Quiet Deliveries Good Practice Guidance' in April 2014. This guidance provides best practice principles for the movement of freight and logistics.
- 2.2.2 The guidance suggests deliveries / collections should be undertaken outside of the main peak periods. In doing so, the contractor can help to reduce the impact of construction traffic on the local highway network, improve road safety and air quality, reduce carbon emissions and enhance the local community. Practical measures which can be implemented during construction include but are not limited to:

General Servicing Best Practice

- Using newer and quieter delivery vehicles and equipment;
- Making sure all equipment is in good working order and maintained to minimise noise;
- Ensuring all staff involved in delivery activity are briefed and trained appropriately, in accordance with the code of practice; and
- Ensuring all construction supply chain providers receive copies of the code and are aware of its importance.

The Delivery Area

- Identify timings for deliveries in advance so both the driver and site operatives are prepared for the arrival;

- Seek to ensure that delivery vehicles spend as little time as possible attempting to access the loading/unloading area, possibly tasking site staff to ensure that manoeuvring can be accomplished safely and quickly; and
- Engines should be switched off when not manoeuvring.


2.2.3 This CTMP has been informed by the policy and guidance noted above and aims to promote best practice sustainable construction methods.

3. Existing Context

3.1 Site Location

3.1.1 Hatch End Industrial Estate is situated in Middle Aston in Oxfordshire, to the west of Fir Lane. The location of the site in the context of the surrounding area, as well as the local transport network is illustrated on **Figure 3.1**.

Figure 3.1 Site Location and Local Amenities

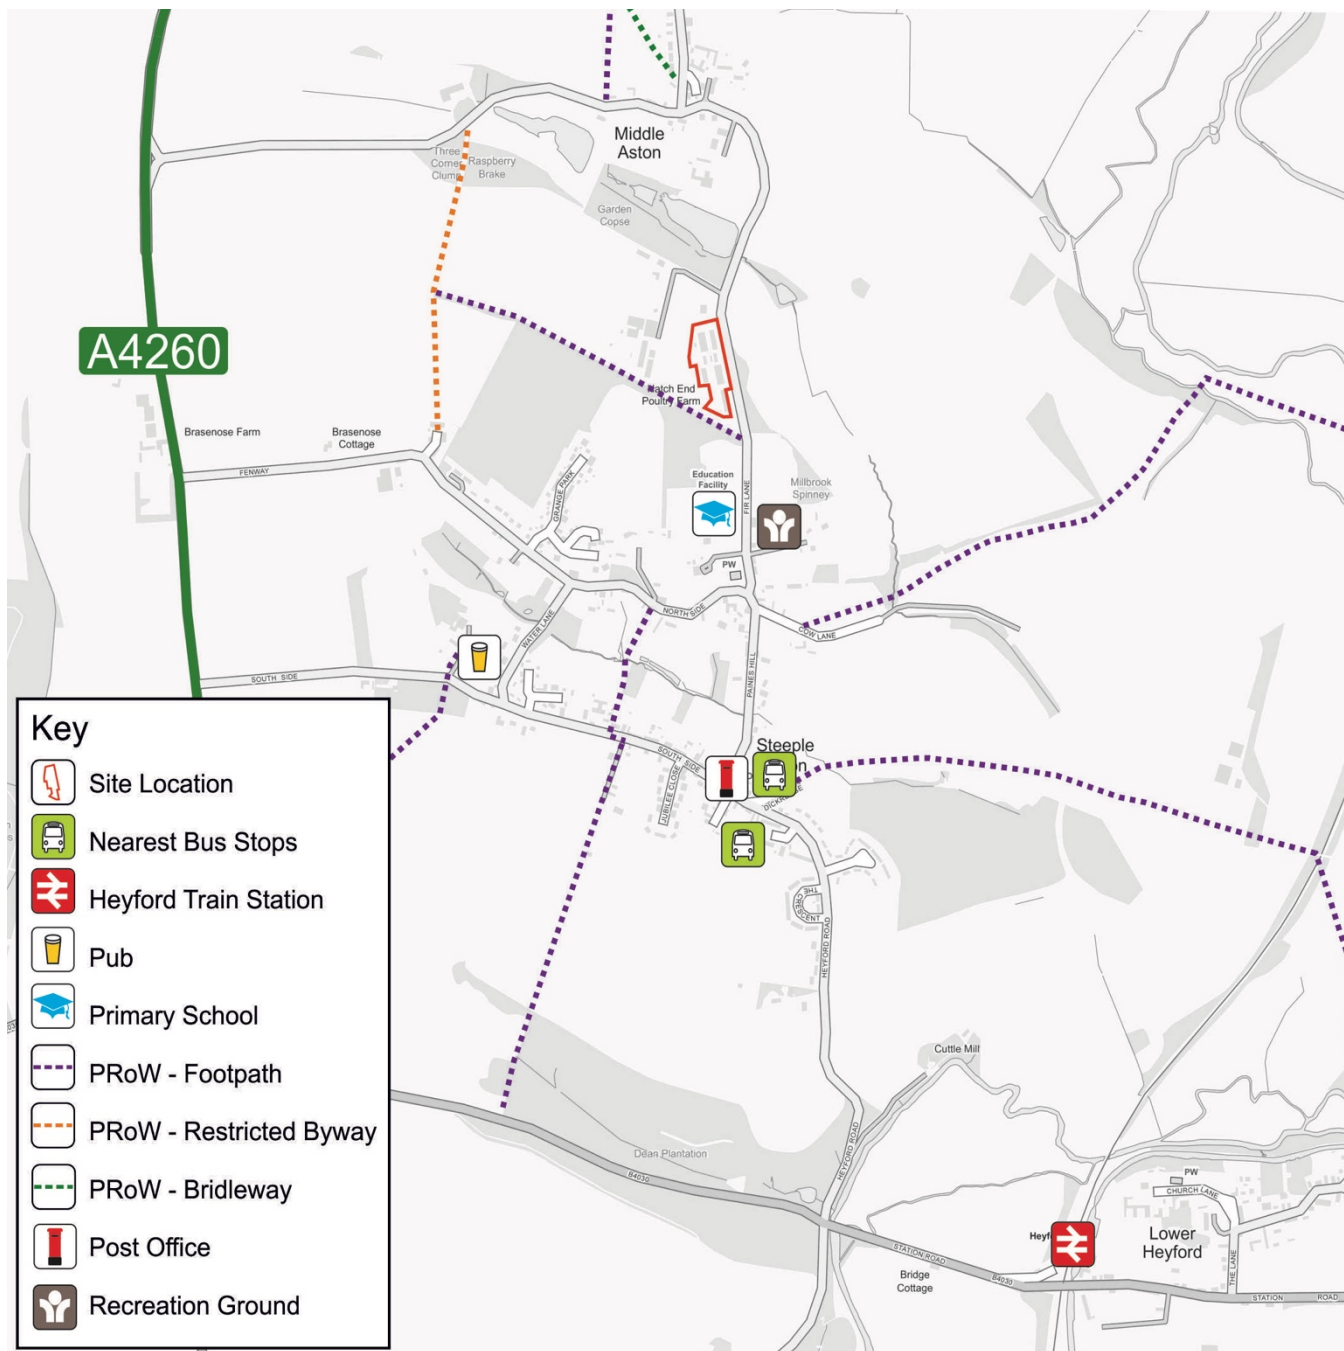

3.2 Local Highway Network

- 3.2.1 Fir Lane is a single-carriageway road, running from its junction with Middle Aston Road to the north to merge with Paines Hill to the south. A 60 miles per hour (mph) speed limit is present along the site frontage and the existing access, reducing to 30mph approximately 160 metres (m) south of the site continuing into the centre of Steeple Aston.
- 3.2.2 As Fir Lane Merges into Paines Hill, North Side connects to Paines Hill to the west. North Side runs westward, merging into Fenway to connect to the A4260 Oxford Road to the west.
- 3.2.3 In the centre of Steeple Aston, Paines Hills connects with South Side. To the west of the junction South Side connects to the A4260 Oxford Road and to the east merges into Heyford Road to connect to the B4030 Station in Heyford.
- 3.2.4 Further detail on the movement of construction traffic to / from the site by appropriate routes is provided in [Section 5](#).

3.3 Sustainable Travel Opportunities

- 3.3.1 The development site is accessible on foot, bicycle and by local bus services. Train services are accessible from Heyford Railway station to the southeast of the site. During the construction programme, on-site workers and contractors will be encouraged to travel to and from the site by sustainable modes to minimise work-related vehicle-related trips.

Walking and Cycling

- 3.3.2 Existing footway provision on both sides of the Fir Lane carriageway begins approximately 310m south from the existing site access, in proximity to Dr Radcliffe's Church of England Primary School. Footway provision continues southwards as Fir Lane adjoins with Paines Hill providing pedestrian access into Steeple Aston, situating local facilities and amenities.
- 3.3.3 A crossing opportunity with tactile paving with dropped kerbs is present as Paines Hill connects with South Side, running on a west to southeast axis. To the east South Side merges with Heyford Road, situating bus stops on both sides of the carriageway and providing for pedestrian access east and west.
- 3.3.4 A number of Public Rights of Way (PRoW) footpaths, byways and bridleways (as presented on the OCC interactive map) are present in proximity to the application site. This includes Footpath 364/5/10 running adjacent to the southern boundary of the site. These PRoWs provide the opportunity for pedestrian access into Middle Aston to the north and Steeple Aston.

Public Transport Services

- 3.3.5 The development proposals are located as to enable bus connectivity with the wider Oxfordshire area including Chipping Norton, Bicester, Banbury and Oxford. In addition, train services from Heyford Railway Station will enable connections from a wider region. These may offer staff the ability to commute by bus or train, if preferred over walking or cycling locally, or over greater distances where bus or train provide a practical alternative to the private car.
- 3.3.6 The nearest bus stops to the application site are the 'Post Office' bus stops, situated on both sides of Heyford Road in Steeple Aston, approximately 980m southeast from the site.
- 3.3.7 The nearest train station to the development site is Heyford Railway Station, situated approximately 2.3 kilometres (km) southeast from the site. Heyford Railway Station provides for train services operated by Great Western Railway and Chiltern Railways. Corresponding train services are available to and from stations including Oxford, Banbury and Didcot Parkway (with subsequent or preceding changes available to and from wider destinations).
- 3.3.8 The above train connections are expected to benefit both staff and visitors for medium to long distances travelled. This will enable visitors throughout the UK to travel to and the from utilising sustainable modes of travel.

4. Construction Activity

4.1 Overview

- 4.1.1 This section identifies the core construction-related activity and arrangements of the site to facilitate the necessary management of construction activity.

4.2 Access to the Site

- 4.2.1 A temporary construction road onto Fir Lane will be formed to the west of the existing access to serve the construction programme at Hatch End Industrial Estate. The temporary construction road will be used for access and egress movements. The definitive location and width of the temporary access road will be confirmed a later stage by the Main Contractor (or a representative of) and agreed with OCC accordingly. This will ensure that all appropriate vehicles used in the construction activity will be able to safely access and egress the construction compound onto the Fir Lane carriageway.
- 4.2.2 It is anticipated that appropriate signage will be placed at the temporary construction road site access to help to deter unauthorised access by non-construction-related traffic or persons.

4.3 Site Staff

- 4.3.1 The Main Contractor (or a representative of) will likely act as the Site Supervisor and oversee demolition and construction activity on-site. This will include managing construction traffic movements in line with this CTMP. The Site Supervisor will liaise with sub-contractors, third-party suppliers and the local community in regard to construction activity throughout the construction programme.
- 4.3.2 The number of construction staff on-site at any one time is likely to fluctuate during over the course of the construction programme. Typically, a maximum of 15 construction staff will be expected to be based on-site at any one time.

4.4 Schedule of Works

- 4.4.1 The expected schedule of works to complete the site's redevelopment is anticipated to occur over a total of 13 weeks. This schedule and corresponding type of work will be finalised by the Main Contractor at a later stage. An indicative schedule of works is provided in **Table 4.1**.

Table 4.1 Indicative Schedule of Works

Duration	Schedule of Works
1 Week	Site Set-Up
1 Week	Demolition Works

8 Weeks

Main Works

3 Weeks

External Works

4.5 Construction Activity Time Periods

4.5.1 The expected hours of construction activity are:

- Monday to Friday between 08:00 – 17:00 hours; and
- Saturday 08:00 – 17:00 hours.

4.5.2 No working is expected on Sundays or Bank Holidays.

4.5.3 Alongside the continued management of construction traffic, deliveries will not be permitted to access the site during the highway network peak hours.

4.6 Delivery / Collection Management

4.6.1 Following best practice guidance, a 'turn-up and go' management regime will be implemented at the site for deliveries and collections. The Main Contractor will be responsible for the operation of this regime and will inform third-party suppliers that it is in place. This management regime will encourage pre-arranging deliveries and give a specific time window to unload/load on-site so only a single delivery / collection vehicle is utilising the access at any one time. The use of freight operators who are accredited by the Fleet Operators Recognition Scheme (FORS) will be encouraged.

4.6.2 It is anticipated that there will be periods within the construction programme where the number of construction vehicles movements to the site will be higher than others. The Main Contractor will work to pre-plan vehicle movements during these peak construction traffic periods. If necessary, fully trained banksmen will be utilised to manage the movement of construction traffic during these peak construction traffic periods. This should ensure the temporary construction access is utilised by one construction vehicle at a time based on pre-arranged delivery slots. If a vehicle has to wait on the highway for a short period of time, this will be required to wait in a safe and respectful manner, avoiding blocking junction sight lines, driveways or footways.

4.7 Construction Staff Car Parking

4.7.1 The available on-site space will be maximised to enable the efficient management of construction activities such as site deliveries, turning facilitates and storage of materials, also enabling staff car parking for construction staff to be provide on-site.

- 4.7.2 Construction staff will be made aware by the Main Contractor before commencing that on-site parking is available on-site, whilst also being encouraged to access the site by sustainable travel modes. As noted in [Section 3](#), the site and surrounding area is accessible by existing pedestrian and cycling infrastructure as well as public transport services. The Main Contractor (and/or Site Supervisor) will be responsible for all staff car parking to check that vehicles do not block areas of the site that need to be accessed, or indeed the temporary construction road.

4.8 Trip Generation

- 4.8.1 The movement of construction staff and sub-contractors to and from the site has potential to generate some vehicular trips. It is anticipated that a maximum of 4 two-way daily vehicular trips will occur throughout the construction programme.

5. Construction Traffic Management

5.1 Overview

- 5.1.1 Construction activity can generate a number of vehicle movements that require management and checking to mitigate and minimise the impact of construction activity on the site operation and also on the surrounding public highway.


5.2 Vehicle Activity and Routing

- 5.2.1 The majority of construction vehicles are likely to be flatbed trucks, typically rigid 7.5t vehicles, with occasional larger articulated HGVs that may be required to deliver or collect materials to the site.
- 5.2.2 To manage construction traffic, both LGVs and HGVs accessing the site will ensure that they do not travel on inappropriate roads, using only construction vehicle access routes that have been identified. These identified routes have been informed by the existing highway conditions, including any restrictions which may impact the movement of HGVs and the potential types of vehicles to be used during construction.
- 5.2.3 The intention of the identified routes is to provide as direct as possible a route to / from the site to the wider strategic road network. The suggested routes should cater for local construction traffic destinations as well as longer distance regional / national construction traffic.

Suggested Construction Vehicle Routes

- 5.2.4 The A4260 to the west of the site provides a link northward towards Banbury and southwards towards Oxford. The main delivery hub of the Hawkins Group, anticipated to be used, is situated in Banbury.
- 5.2.5 To access the A4260 from the site, the preferred routing option is to travel southwards on Fir Lane/Paines Hill and then turn right onto South Side to join the A4260 Oxford Road. The same route in reverse allows access to the site from the A4260 Oxford Road. An alternative route to and from the A4260 Oxford Road would be to travel south from the site along Fir Lane and then turn right onto North Side to connect to the A4260 Oxford Road.
- 5.2.6 An 'unsuitable for HGVs' sign is present on the junction between the A4260 Oxford Road and the unnamed road running from Middle Aston Road, after it merges with Fir Lane. Construction vehicles will not use this road or junction to access the site from the A4260 Oxford Road.
- 5.2.7 The suggested preferred and alternative construction routes are illustrated on **Figure 5.1**.

Figure 5.1 Preferred and Alternative Construction Route

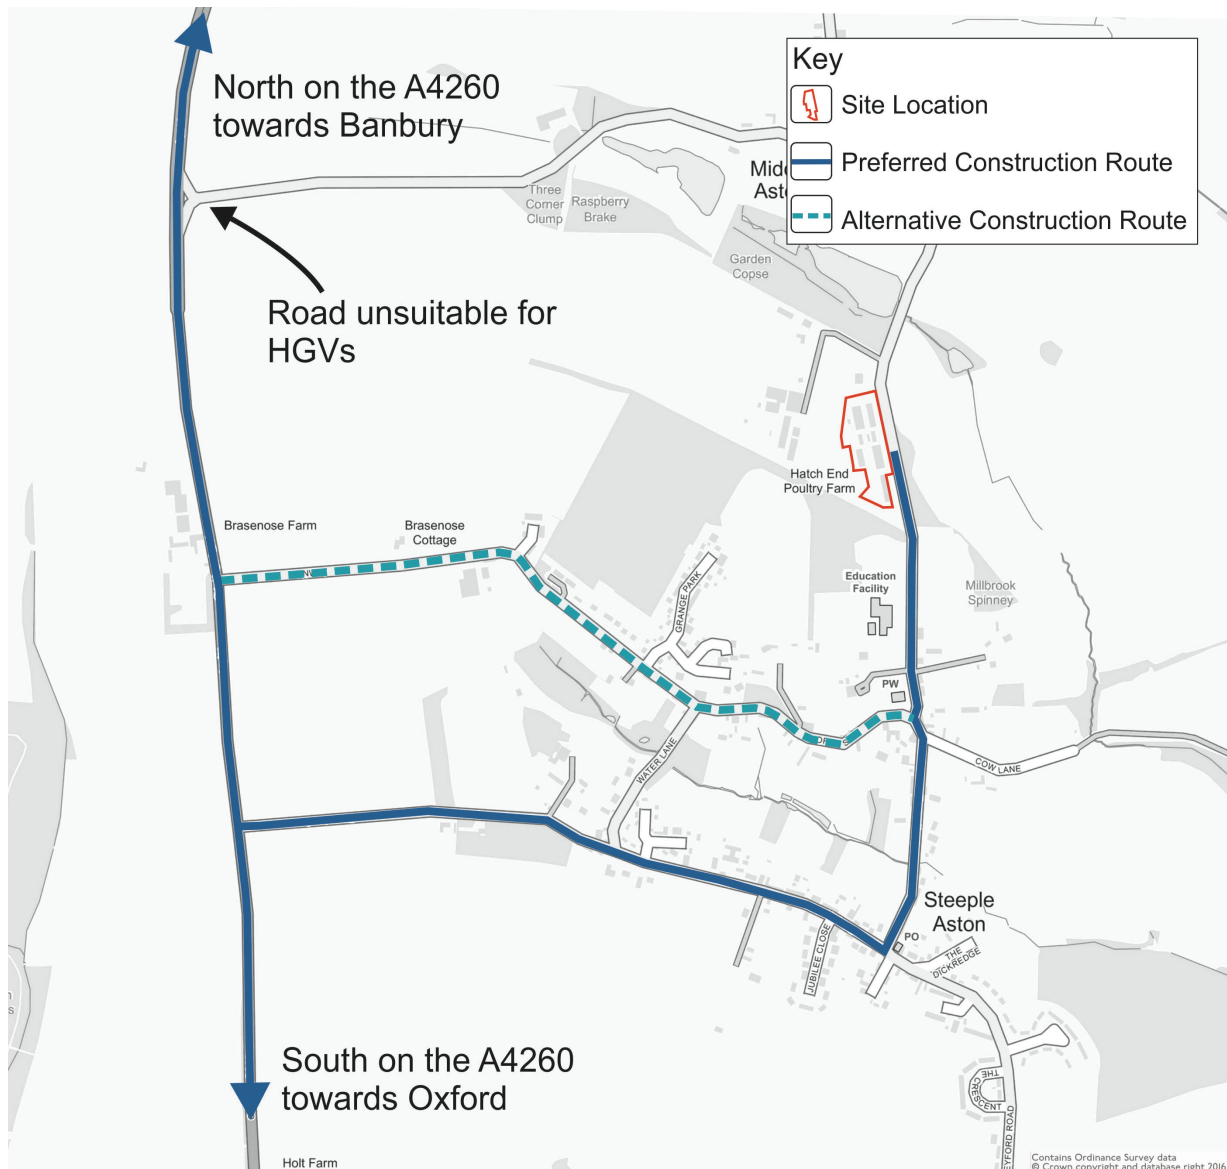

5.2.8 All HGV construction traffic will be encouraged to use the suggested preferred route. Where appropriate considering the expected vehicle type, destination and time of day smaller construction vehicles could also be directed to the alternative construction route.

6. Mitigation Measures

6.1 Overview

6.1.1 This section details mitigation measures to minimise the impact of construction traffic on the surrounding local highway network. These measures would be expected to be implemented by the Main Contractor at the appropriate time in the construction programme and all sub-contractors and construction personal would be expected to follow each measure, where applicable.

6.2 General Servicing Best Practice

General Best Practice

6.2.1 In accordance with the DfT's best practice on servicing sites, the following practice would be encouraged for all activity at the site:

- Making sure all equipment is in good working order and maintained to minimise noise;
- Ensuring all construction staff involved in delivery activity are briefed and trained appropriately, and where necessary banksmen are used to manage construction traffic; and
- Ensuring all construction supply chain providers are aware of the expected best practice measures.

Delivery Management

- Identify timings for deliveries in advance so both the driver and site operators are prepared for the arrival;
- Seek to ensure that delivery vehicles spend as little time as possible accessing the loading and unloading areas, with the use of banksmen to manage vehicle movements; and
- Engines should be switched off immediately when not manoeuvring.

6.3 Materials Storage and Security

6.3.1 The main contractor will be encouraged to adopt a 'call off' approach where only materials immediately required to meet the programme would be stored on site, allowing for planned and managed deliveries. This may include off-site assembly of some components.

6.4 Local Community Liaison

6.4.1 As the construction site is in proximity to residential areas in Steeple Aston and Middle Aston, continued interaction with the local community will be encouraged. As construction progresses, the Main Contractor will seek to regularly inform local residents of progress and the associated timescales.

6.5 Noise and Vibration Management

- 6.5.1 The Main Contractor will ensure mitigation measures are put in place to minimise the impact of noise and vibrations during demolition and construction. Following best practice guidance, machinery used on-site should be in good working condition and well maintained.
- 6.5.2 When a vehicle is stationary, its engine will be turned off for the duration of its time on-site, unless its engine is required.

6.6 Vehicle Checks

- 6.6.1 The Main Contractor will ensure best practice guidance is followed to help ensure the impact of construction activity is minimised. The access will be kept clear of mud and debris throughout the programme. Construction vehicles leaving the site will be checked before accessing the highway onto Fir Lane.

7. Monitoring and Review

- 7.1.1 This CTMP is a live document and will be reviewed and updated by the Main Contractor on a regular basis, if and where necessary. The Main Contractor will be the first point of contact regarding construction traffic management and the site operation.
- 7.1.2 If appropriate, The Main Contractor will liaise with Cherwell District Council and / or OCC to provide regular updates on the implementation of the CTMP and its effectiveness.

8. Summary

8.1 Overview

8.1.1 This CTMP has been prepared to detail the expected construction programme for the redevelopment of Hatch End Industrial Estate in Middle Aston, Oxfordshire.

8.1.2 This CTMP outlines methods to keep construction vehicle activity to an efficient and manageable number of journeys to and from the site. Vehicle access to the construction site is constrained and the construction programme has been designed to take account of this by utilising modern small module building techniques to reduce the number of larger construction vehicles.

8.1.3 The principle issues addressed within the CTMP are as follows:

- Schedule of works;
- Deliveries and hours of operations;
- Routing of construction traffic and delivery vehicles; and
- Proposed Mitigation Measures.

8.1.4 This CTMP aims to minimise the impact of construction vehicle movements in line with guidance published by DfT and OCC.

APPENDICES

Middle Aston Limited

Hatch End Industrial Estate, Middle Aston

Construction Traffic Management Plan

mode

transport planning

APPENDIX A


Proposed Site Layout

This drawing is the copyright of ngarchitecture. It may not be copied or disclosed to any third party for any purpose except as authorised in writing by ngarchitecture.

Do not scale this drawing. Figured dimensions only are to be used in preference to small scale drawings. All dimensions are to be checked on site before work proceeds. Any errors or omissions are to be reported to ngarchitecture. If in doubt ask.

The contractor is to provide full sized setting out drawings based on information contained in this drawing for ngarchitecture to approve prior to commencing manufacture.

This drawing is to be read in conjunction with all the relevant consultants and / or specialist drawings or documents and any discrepancies or variations are to be notified to ngarchitecture before the affected work commences.

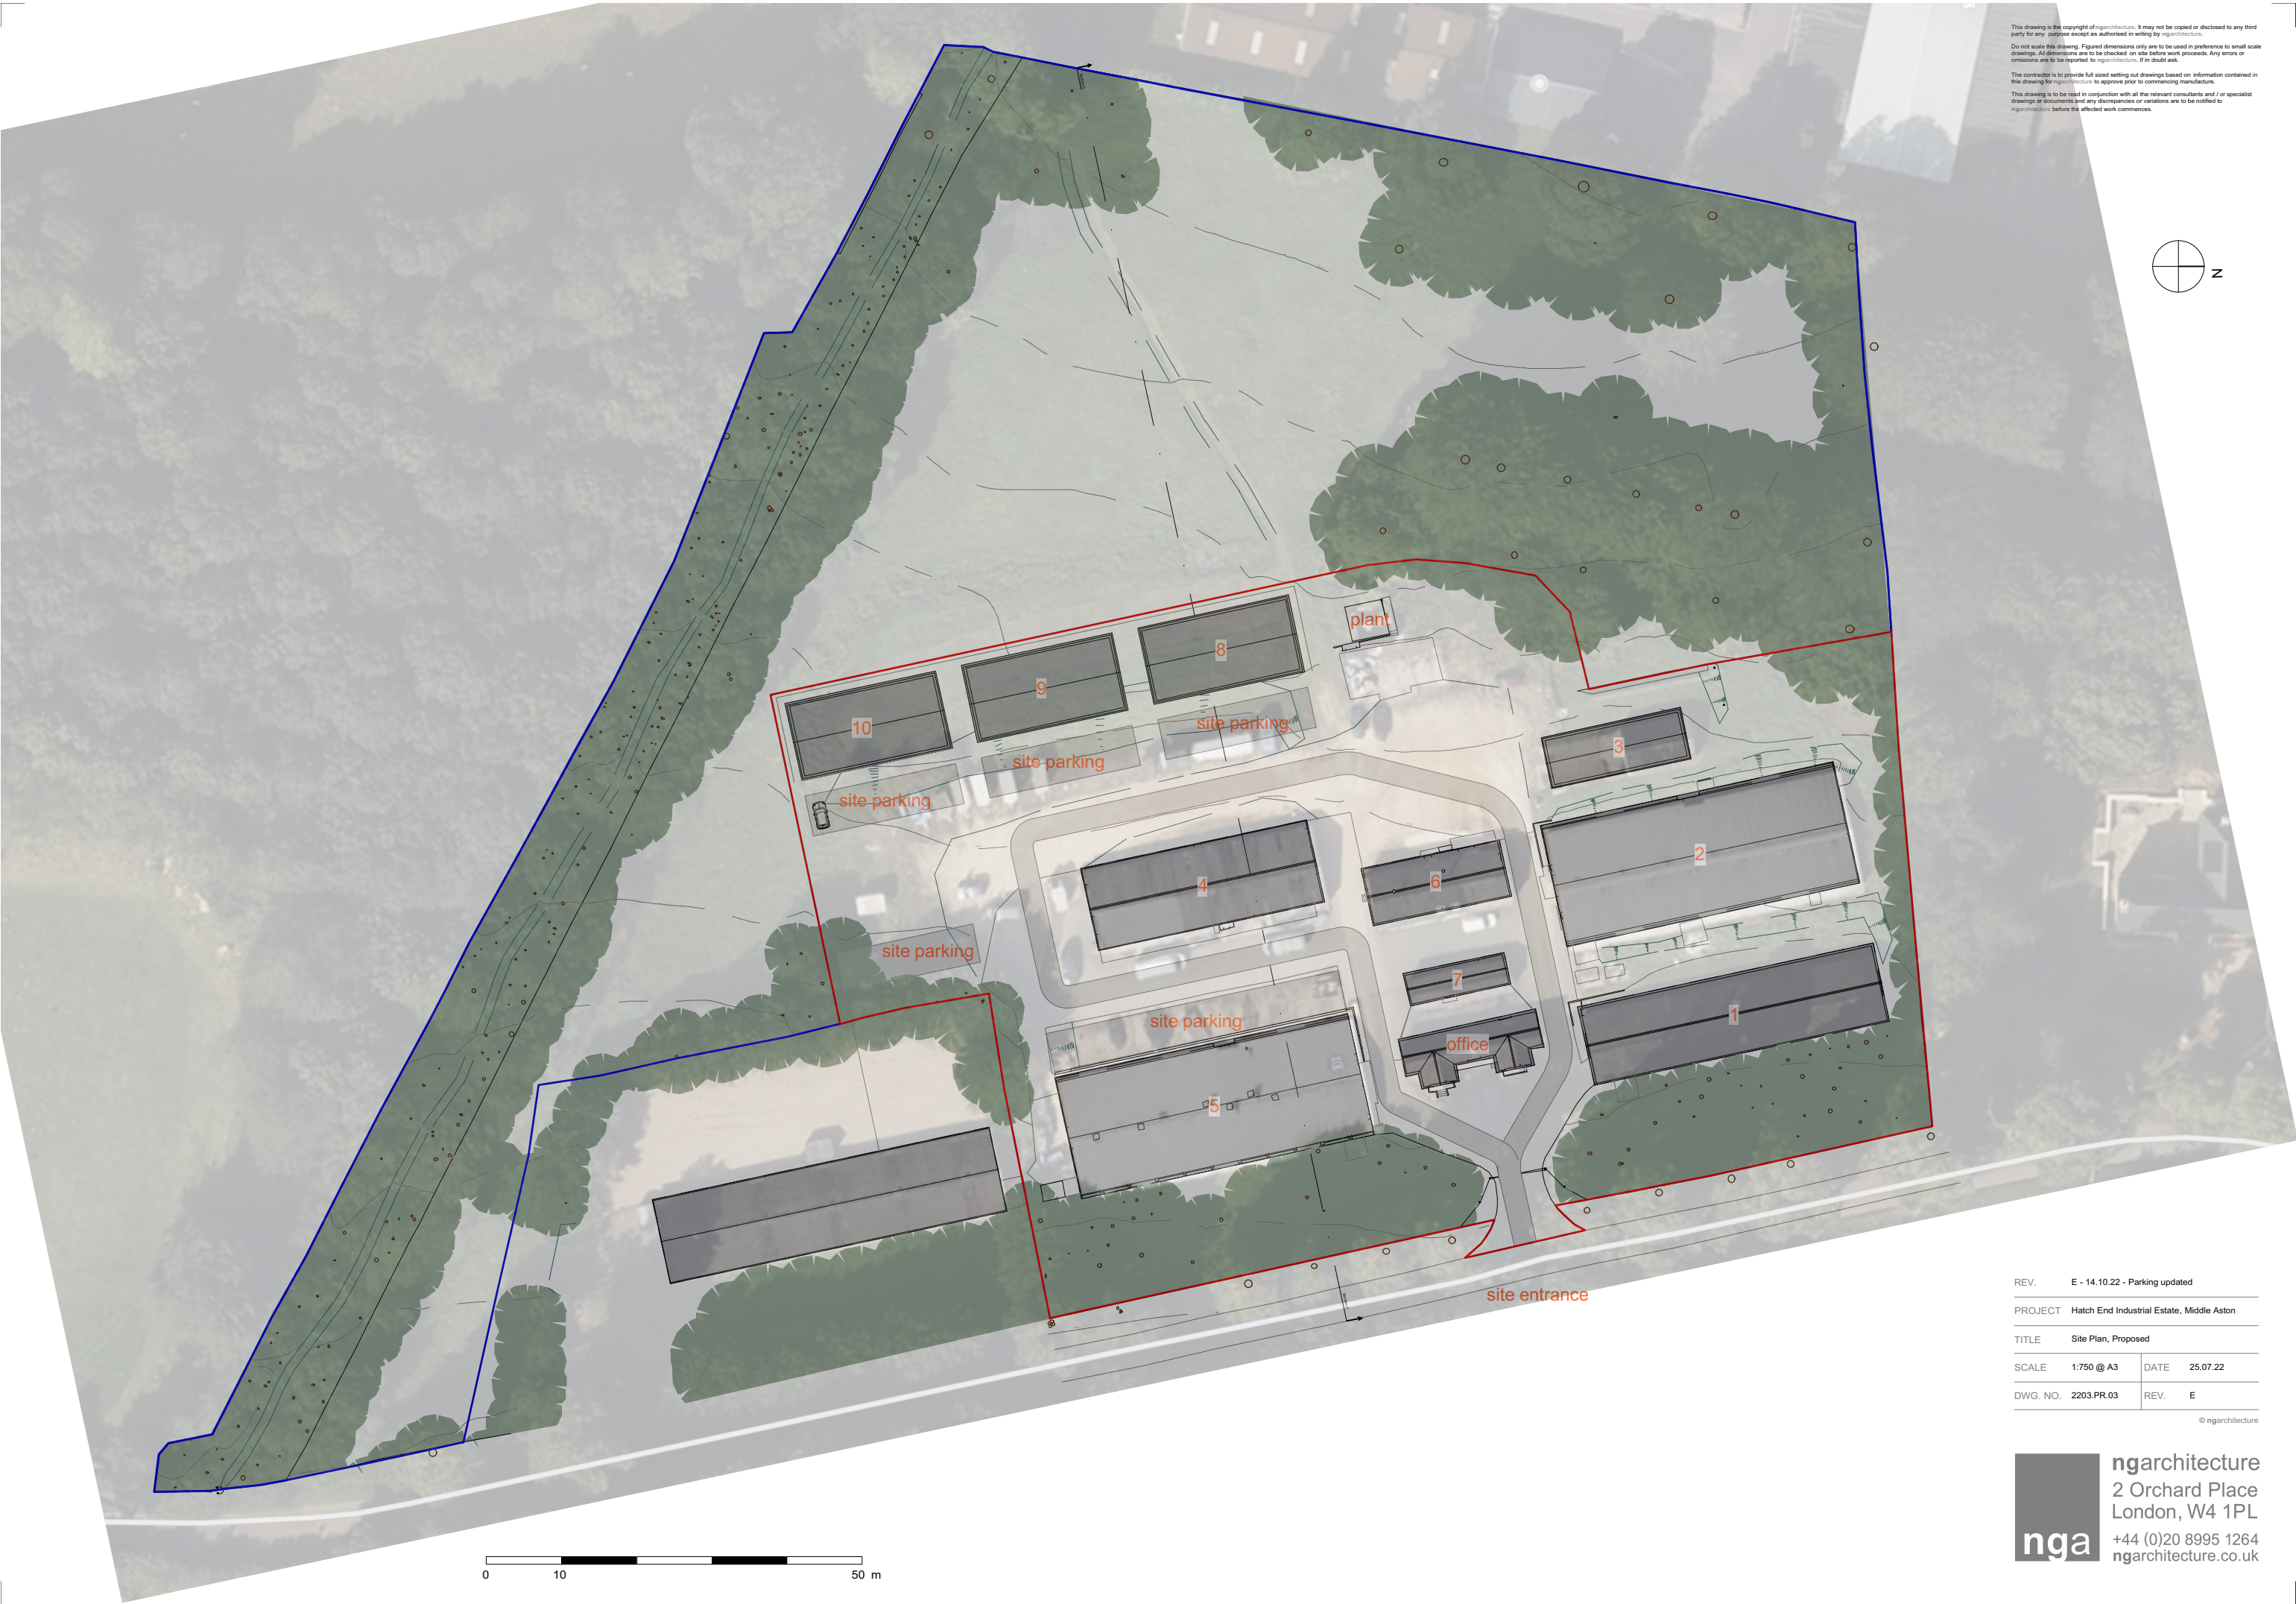

REV.	E - 14.10.22 - Parking updated		
PROJECT	Hatch End Industrial Estate, Middle Aston		
TITLE	Site Plan, Proposed		
SCALE	1:750 @ A3	DATE	25.07.22
DWG. NO.	2203.PR.03	REV.	E

© ngarchitecture

This drawing is the copyright of ngarchitecture. It may not be copied or disclosed to any third party for any purpose except as authorised in writing by ngarchitecture.

Do not scale this drawing. Figured dimensions only are to be used in preference to small scale drawings. All dimensions are to be checked on site before work proceeds. Any errors or omissions are to be reported to ngarchitecture. If in doubt ask.

The contractor is to provide full sized setting out drawings based on information contained in this drawing for ngarchitecture to approve prior to commencing manufacture.

This drawing is to be read in conjunction with all the relevant consultants and / or specialist drawings or documents and any discrepancies or variations are to be notified to ngarchitecture before the affected work commences.



gabion retaining wall

gabion retaining wall

Unit 10

Unit 9

Unit 8

parking

parking

parking

road

Unit 4

parking

0 1 5

REV.	A - 14.10.22 - General amendments		
PROJECT	Hatch End Industrial Estate, Middle Aston		
TITLE	Shed Plan, Proposed		
SCALE	1:200 @ A3	DATE	04.10.22
DWG. NO.	2203.PR.05	REV.	A

© ngarchitecture

ngarchitecture
2 Orchard Place
London, W4 1PL
nga +44 (0)20 8995 1264
ngarchitecture.co.uk



keep up with mode:



Birmingham

☎ 0121 794 8390

London

☎ 020 7293 0217

Manchester

☎ 0161 464 9495

Reading

☎ 0118 211 8180
