



Taylor Wimpey

Chesterton

Factual soakaway test report

313035-02 (00)

AUGUST 2015

RSK



RSK GENERAL NOTES

Project No.: 313035-02(00)



Title: Factual soakaway test report: Chesterton


Client: Taylor Wimpey (Oxfordshire)

Date: 4th August 2015

Office: Abbey Park, Humber Road, Coventry, CV3 4AQ. Tel: 02476 505600

Status: Final

Author	<u>Adam Jones</u>	Approved by	<u>Marc Dixon</u>
Signature		Signature	
Date:	<u>4th August 2015</u>	Date:	<u>4th August 2015</u>

Project manager	<u>Michael Lawson</u>
Signature	
Date:	<u>4th August 2015</u>

RSK Environment Limited (RSK) has prepared this report for the sole use of the client, showing reasonable skill and care, for the intended purposes as stated in the agreement under which this work was completed. The report may not be relied upon by any other party without the express agreement of the client and RSK. No other warranty, expressed or implied, is made as to the professional advice included in this report.

Where any data supplied by the client or from other sources have been used, it has been assumed that the information is correct. No responsibility can be accepted by RSK for inaccuracies in the data supplied by any other party. The conclusions and recommendations in this report are based on the assumption that all relevant information has been supplied by those bodies from whom it was requested.

No part of this report may be copied or duplicated without the express permission of RSK and the party for whom it was prepared.

Where field investigations have been carried out, these have been restricted to a level of detail required to achieve the stated objectives of the work.

This work has been undertaken in accordance with the quality management system of RSK Environment Ltd.

CONTENTS

1 INTRODUCTION.....	2
1.1 Objective and scope of investigation	2
1.2 Limitations	2
2 TEST PROCEEDURE AND RESULTS.....	3

FIGURES

Figure 1	Site location plan
Figure 2	Test location plan

APPENDICES

Appendix A	Service constraints
Appendix B	Exploratory hole records
Appendix C	Test records

1 INTRODUCTION

RSK Environment Limited (RSK) have been commissioned by Taylor Wimpey (Oxfordshire) (the Client) to carry out a series of shallow infiltration tests at a site off The Hale, Chesterton.

The investigation was undertaken in accordance with the instructions provided by RPS Planning and Development (the Engineer), on behalf of the Client. This report summarises the work undertaken and presents the data obtained.

This report is subject to the RSK service constraints given in Appendix A.

1.1 Objective and scope of investigation

The objective of the investigation was to provide information regarding the infiltration characteristics of the shallow soils, in order to inform the design of the proposed residential development.

The project was carried out to an agreed brief as set out in RSK's proposal (313035-T00(00), dated 30th June 2015). The scope of testing was as follows:

- Excavate 5 trial holes into the Cornbrash Formation to depths of between 0.70m and 1.50m bgl (i.e. the maximum depths of the proposed soakaways); and
- Undertake three soakage tests to full BRE specification at each location to assess infiltration characteristics.

A description of the procedures followed during the testing are presented within Section 3. The exploratory hole records are presented in Appendix B, while factual data obtained during the soakaway tests is presented within Appendix C of this report.

1.2 Limitations

The comments provided and the opinions expressed within this report are based on the ground conditions encountered during the intrusive investigation, and on the results of testing undertaken in-situ and in the laboratory. There may, however, be conditions pertaining to the site that have not been disclosed by the investigation; and therefore could not be taken into account. In particular, it should be noted that the thickness and quality of the made ground may be variable across the site. In addition, groundwater levels and ground gas concentrations and flows may vary from those reported due to seasonal, or other, effects.

2 TEST PROCEDURE AND RESULTS

Soakaway testing was undertaken in accordance with the instructions of the Client and Engineer between 20th and 22nd July 2015.

The techniques adopted for the intrusive investigation were chosen based on the aims of the investigation, and the access constraints for plant and equipment.

The testing strategy was primarily focused on the characterisation of the shallow Cornbrash Formation; in order to confirm the infiltration characteristics of the formation. The testing was undertaken at the locations and depths specified by the Engineer.

The investigation and the soil descriptions were carried out in accordance with 'BS 5930:1999. Code of Practice for Site Investigations' (BSI, 1999); and the testing was undertaken in accordance with Building Research Establishment (BRE) 365.

Each soakaway trial pit was excavated and logged by a suitably qualified engineer, with full logs for each location presented within Appendix B.

Table 1 below, summarises the programme of testing undertaken and the infiltration rates recorded for each individual test. The results of the tests are presented in full within Appendix C.

Table 1: Summary of infiltration testing programme


Location	Soakaway Depth (m bgl)	Stratum	Result (m/s)
TP09	1.20	Cornbrash Formation (limestone and clayey sand)	9.90×10^{-6}
			3.89×10^{-6}
			7.57×10^{-6}
TP10	1.20	Cornbrash Formation (limestone)	2.41×10^{-4}
			1.59×10^{-4}
			5.74×10^{-5}
TP11	1.10	Cornbrash Formation (limestone)	1.68×10^{-5}
			1.14×10^{-5}
			1.17×10^{-5}
TP12	0.70	Cornbrash Formation (limestone)	1.25×10^{-4}
			1.05×10^{-4}
			7.52×10^{-5}
TP13	0.90	Cornbrash Formation (limestone and clayey sand)	1.01×10^{-4}
			8.97×10^{-5}
			7.73×10^{-5}

As can be seen from the above, infiltration rates within the Cornbrash Formation ranged between 2.41×10^{-4} m/s and 3.89×10^{-6} m/s. Infiltration rates were typically recorded at 10^{-4} m/s or 10^{-5} m/s, while infiltration rates noted in TP09 were typically 10^{-6} m/s.

FIGURES



 Indicative site boundary


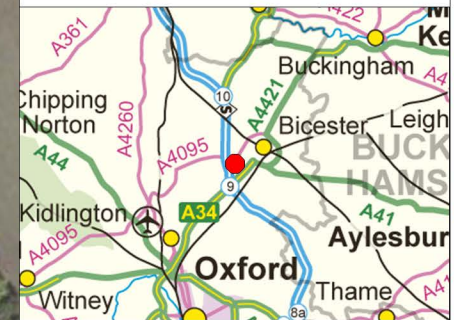


Rev	Date	Description	Drn	Chk	App
00	22.05.15	313035	RG	SP	AJ

Chesterton



Figure 1
Site Location Plan





- Indicative site boundary
- + CBR
- ⊕ Foundation pit
- X Trial pit
- X Trial pit and soakaway
- ▲ Window sample




Rev	Date	Description	Drn	Chk	App
01	23.07.15	313035	RG	SP	AJ

Chesterton



Figure 2
Exploratory Hole Location Plan



APPENDIX A

SERVICE CONSTRAINTS

1. This report and the site investigation carried out in connection with the report (together the "Services") were compiled and carried out by RSK Environment Limited (RSK) for Redrow Homes Midlands (the "client") in accordance with the terms of a contract between RSK and the "client", dated 18th June 2015. The Services were performed by RSK with the skill and care ordinarily exercised by a reasonable environmental consultant at the time the Services were performed. Further, and in particular, the Services were performed by RSK taking into account the limits of the scope of works required by the client, the time scale involved and the resources, including financial and manpower resources, agreed between RSK and the client.
2. Other than that expressly contained in paragraph 1 above, RSK provides no other representation or warranty whether express or implied, in relation to the Services.
3. Unless otherwise agreed the Services were performed by RSK exclusively for the purposes of the client. RSK is not aware of any interest of or reliance by any party other than the client in or on the Services. Unless expressly provided in writing, RSK does not authorise, consent or condone any party other than the client relying upon the Services. Should this report or any part of this report, or otherwise details of the Services or any part of the Services be made known to any such party, and such party relies thereon that party does so wholly at its own and sole risk and RSK disclaims any liability to such parties. **Any such party would be well advised to seek independent advice from a competent environmental consultant and/or lawyer.**
4. It is RSK's understanding that this report is to be used for the purpose described in the introduction to the report. That purpose was a significant factor in determining the scope and level of the Services. Should the purpose for which the report is used, or the proposed use of the site change, this report may no longer be valid and any further use of or reliance upon the report in those circumstances by the client without RSK 's review and advice shall be at the client's sole and own risk. Should RSK be requested to review the report after the date hereof, RSK shall be entitled to additional payment at the then existing rates or such other terms as agreed between RSK and the client.
5. The passage of time may result in changes in site conditions, regulatory or other legal provisions, technology or economic conditions which could render the report inaccurate or unreliable. The information and conclusions contained in this report should not be relied upon in the future without the written advice of RSK. In the absence of such written advice of RSK, reliance on the report in the future shall be at the client's own and sole risk. Should RSK be requested to review the report in the future, RSK shall be entitled to additional payment at the then existing rate or such other terms as may be agreed between RSK and the client.
6. The observations and conclusions described in this report are based solely upon the Services which were provided pursuant to the agreement between the client and RSK. RSK has not performed any observations, investigations, studies or testing not specifically set out or required by the contract between the client and RSK. RSK is not liable for the existence of any condition, the discovery of which would require performance of services not otherwise contained in the Services. For the avoidance of doubt, unless otherwise expressly referred to in the introduction to this report, RSK did not seek to evaluate the presence on or off the site of asbestos, electromagnetic fields, lead paint, heavy metals, radon gas or other radioactive or hazardous materials.
7. The Services are based upon RSK's observations of existing physical conditions at the Site gained from a walk-over survey of the site together with RSK's interpretation of information including documentation, obtained from third parties and from the client on the history and usage of the site. The Services are also based on information and/or analysis provided by independent testing and information services or laboratories upon which RSK was reasonably entitled to rely. The Services clearly are limited by the accuracy of the information, including documentation, reviewed by RSK and the observations possible at the time of the walk-over survey. Further RSK was not authorised and did not attempt to independently verify the accuracy or completeness of information, documentation or materials received from the client or third parties, including laboratories and information services, during the performance of the Services. RSK is not liable for any inaccurate information or conclusions, the discovery of which inaccuracies required the doing of any act including the gathering of any information which was not reasonably available to RSK and including the doing of any independent investigation of the information provided to RSK save as otherwise provided in the terms of the contract between the client and RSK.
8. The phase II or intrusive environmental site investigation aspects of the Services is a limited sampling of the site at pre-determined borehole and soil vapour locations based on the operational configuration of the site. The conclusions given in this report are based on information gathered at the specific test locations and can only be extrapolated to an undefined limited area around those locations. The extent of the limited area depends on the soil and groundwater conditions, together with the position of any current structures and underground facilities and natural and other activities on site. In addition chemical analysis was carried out for a limited number of parameters [as stipulated in the contract between the client and RSK] [based on an understanding of the available operational and historical information,] and it should not be inferred that other chemical species are not present.
9. Any site drawing(s) provided in this report is (are) not meant to be an accurate base plan, but is (are) used to present the general relative locations of features on, and surrounding, the site.



APPENDIX B

EXPLORATORY HOLE RECORDS

Contract: Chesterton		Client: Taylor Winpey Oxfordshire		Trial Pit: TP09
Contract Ref: 313035	Start: 20.07.15 End: 20.07.15	Ground Level: ---	Co-ordinates: ---	Sheet: 1 of 1

Samples and In-situ Tests				Water	Backfill	Description of Strata	Depth (Thickness)	Material Graphic Legend
Depth	No	Type	Results					
						Crop over brown slightly clayey gravelly SAND, with frequent rootlets. Sand is fine to medium. Gravel is subangular fine to medium limestone.	(0.30) 0.30	
						White LIMESTONE recovered as flat angular to subangular cobble sized fragments. Limestone is coarse gravel medium strong to strong.	(0.60) 0.90	
						Yellowish orange clayey slightly gravelly SAND. Sand is fine to medium. Gravel is angular to subangular medium to coarse limestone.	(0.60) 1.50	
						Very stiff grey CLAY.	1.70	

GINT LIBRARY v8.05 - Lib0004 ProjVersion: v8.05 - Core+Logs 0003 | Log TRIAL PIT LOG | 313035 - CHESTERTON PHASE 2.GPJ - v8.05 | 27/07/15 - 16:45 | LM.
RSK Environment Ltd, The Enterprise Centre, Coventry University Technology Park, Coventry, CV1 2TX. Tel: 02476 236816, Fax: 02476 236014, Web: www.rsk.co.uk.

<p>Plan (Not to Scale)</p>	<h3 style="text-align: center;">General Remarks</h3> <ol style="list-style-type: none"> 1. Location scanned with a CAT and Signal Generator prior to breaking ground. 2. Trial pit remained stable during excavation. 3. Groundwater encountered at 1.40m bgl 4. Trial pit filled with flint gravel up to ground level for duration of soakaway testing. 5. Soakaway test carried out at 1.20m bgl 6. Upon completion of three soakaway tests, gravel was removed and excavation continued in order to test the extent of the underlying strata. 7. Trial pit backfilled with arising upon completion.
All dimensions in metres	
Scale: 1:25	
Method Used: Machine dug	Plant Used: JCB-3CX
Logged By: adamjones	Checked By:

Contract: Chesterton		Client: Taylor Winpey Oxfordshire		Trial Pit: TP10
Contract Ref: 313035	Start: 20.07.15 End: 20.07.15	Ground Level: ---	Co-ordinates: ---	Sheet: 1 of 1

Samples and In-situ Tests				Water	Backfill	Description of Strata	Depth (Thickness)	Material Graphic Legend
Depth	No	Type	Results					
0.60	1	B			Grass over brown slightly clayey gravelly SAND with frequent rootlets. Sand is fine to medium. Gravel is subangular fine to medium limestone.	(0.30)	0.30	
					LIMESTONE recovered as flat subangular cobble sized fragments. Limestone is dark grey coarse grained medium strong to strong with layers of sand and gravel. Sand is fine to medium Gravel is subangular fine to coarse of limestone.	(1.45)	1.45	
					Orangish clayey gravelly SAND.	1.75	1.75	
					... Stuff grey clay at base. Trial pit terminated at 1.90m bgl	1.90	1.90	

GINT LIBRARY v8.05 - Lib0004 ProjVersion: v8.05 - Core+Logs 0003 | Log TRIAL PIT LOG | 313035 - CHESTERTON PHASE 2.GPJ - v8.05 | 27/07/15 - 16:45 | LM.
RSK Environment Ltd, The Enterprise Centre, Coventry University Technology Park, Coventry, CV1 2TX. Tel: 02476 236816, Fax: 02476 236014, Web: www.rsk.co.uk.

<p>Plan (Not to Scale)</p>	<h3 style="text-align: center;">General Remarks</h3> <ol style="list-style-type: none"> 1. Location scanned with a CAT and Signal Generator prior to breaking ground. 2. Trial pit remained stable during excavation. 3. Groundwater not encountered. 4. Trial pit filled with flint gravel up to ground level for duration of soakaway testing. 5. Soakaway test carried out at 1.20m bgl 6. Upon completion of three soakaway tests, gravel was removed and excavation continued in order to test the extent of the underlying strata. 7. Trial pit backfilled with arising upon completion.
All dimensions in metres	
Scale: 1:25	
Method Used: Machine dug	Plant Used: JCB-3CX
Logged By: adamjones	Checked By: AGS

Contract: Chesterton		Client: Taylor Winpey Oxfordshire		Trial Pit: TP11	
Contract Ref: 313035		Start: 20.07.15	Ground Level: ---	Co-ordinates: ---	Sheet: 1 of 1
		End: 20.07.15			

Samples and In-situ Tests				Water	Backfill	Description of Strata	Depth (Thickness)	Material Graphic Legend
Depth	No	Type	Results					
1.20	1	B			Grass over brown slightly clayey gravelly SAND with frequent rootlets. Sand is fine to medium. Gravel is subangular fine to medium limestone.	0.20		
					LIMESTONE recovered as flat subangular cobble sized fragments. Limestone is dark grey coarse grained medium strong to strong with layers of sand and gravel. Sand is fine to medium Gravel is subangular fine to coarse of limestone.	(0.90)		
					Yellowish orange clayey SAND with frequent cobbles of limestone.	1.10		
					Stiff grey mottled orange CLAY.	1.30		
					Trial pit terminated at 1.70m bgl	(0.40)		
			1.70					

GIN1 LIBRARY v8.05.GLB.LibVersion: v8.05 - Core+Logs 0003 | Log TRIAL PIT LOG | 313035 - CHESTERTON PHASE 2.GPJ - v8.05 | 27/07/15 - 16:45 | LM.
RSK Environment Ltd, The Enterprise Centre, Coventry University Technology Park, Coventry, CV1 2TX. Tel: 02476 236816, Fax: 02476 236014, Web: www.rsk.co.uk.

<p>Plan (Not to Scale)</p>	<h3 style="text-align: center;">General Remarks</h3> <ol style="list-style-type: none"> 1. Location scanned with a CAT and Signal Generator prior to breaking ground. 2. Trial pit remained stable during excavation. 3. Groundwater not encountered. 4. Trial pit filled with flint gravel up to ground level for duration of soakaway testing. 5. Soakaway test carried out at 1.10m bgl 6. Upon completion of three soakaway tests, gravel was removed and excavation continued in order to test the extent of the underlying strata. 7. Trial pit backfilled with arising upon completion.
All dimensions in metres	
Scale: 1:25	
Method Used: Machine dug	Plant Used: JCB-3CX
Logged By: adamjones	Checked By:

Contract: Chesterton		Client: Taylor Winpey Oxfordshire		Trial Pit: TP12
Contract Ref: 313035	Start: 20.07.15 End: 20.07.15	Ground Level: ---	Co-ordinates: ---	Sheet: 1 of 1

Samples and In-situ Tests				Water	Backfill	Description of Strata	Depth (Thickness)	Material Graphic Legend
Depth	No	Type	Results					
1.20	1	B			Grass over brown slightly clayey gravelly SAND with frequent rootlets. Sand is fine to medium. Gravel is angular to subangular fine to medium limestone.	0.20		
					White LIMESTONE recovered as flat subangular cobble sized fragments. Limestone is dark grey coarse grained medium strong to strong.	(0.90)		
					Yellowish orange clayey SAND.	1.10		
					Stiff grey CLAY.	1.25		
					Trial pit terminated at 1.40m bgl		1.40	

GIN1 LIBRARY v8.05.GLB.LibVersion: v8.05 - Core+Logs 0003 | Log TRIAL PIT LOG | 313035 - CHESTERTON PHASE 2.GPJ - v8.05 | 27/07/15 - 16:45 | LM. RSK Environment Ltd, The Enterprise Centre, Coventry University Technology Park, Coventry, CV1 2TX. Tel: 02476 236816, Fax: 02476 236014, Web: www.rsk.co.uk.

<p>Plan (Not to Scale)</p>	<h3 style="text-align: center;">General Remarks</h3> <ol style="list-style-type: none"> 1. Location scanned with a CAT and Signal Generator prior to breaking ground. 2. Trial pit remained stable during excavation. 3. Groundwater not encountered. 4. Trial pit filled with flint gravel up to ground level for duration of soakaway testing. 5. Soakaway test carried out at 0.70m bgl 6. Upon completion of three soakaway tests, gravel was removed and excavation continued in order to test the extent of the underlying strata. 7. Trial pit backfilled with arising upon completion.
All dimensions in metres	
Scale: 1:25	
Method Used: Machine dug	Plant Used: JCB-3CX
Logged By: adamjones	Checked By: AGS

Contract: Chesterton		Client: Taylor Winpey Oxfordshire		Trial Pit: TP13
Contract Ref: 313035	Start: 20.07.15 End: 20.07.15	Ground Level: ---	Co-ordinates: ---	Sheet: 1 of 1


Samples and In-situ Tests				Water	Backfill	Description of Strata	Depth (Thickness)	Material Graphic Legend
Depth	No	Type	Results					
0.80	1	B			Grass over brown slightly clayey gravelly SAND with frequent rootlets. Sand is fine to medium. Gravel is angular to subangular fine to medium limestone.	0.20		
					LIMESTONE recovered as flat subangular cobble sized fragments. Limestone is dark grey coarse grained medium strong to strong with layers of sand and gravel. Sand is fine to medium Gravel is subangular fine to coarse of limestone.	(0.50)		
					Yellowish orange clayey slightly gravelly fine to medium SAND. Gravel is angular to subangular medium to coarse limestone.	(0.40)		
						1.10		

GINT LIBRARY v8.05 - Lib0004 ProjVersion: v8.05 - Core+Logs 0003 | Log TRIAL PIT LOG | 313035 - CHESTERTON PHASE 2.GPJ - v8.05 | 27/07/15 - 16:45 | LM.
RSK Environment Ltd, The Enterprise Centre, Coventry University Technology Park, Coventry, CV1 2TX. Tel: 02476 236816, Fax: 02476 236014, Web: www.rsk.co.uk.

<p>Plan (Not to Scale)</p>	<h3 style="text-align: center;">General Remarks</h3> <ol style="list-style-type: none"> 1. Location scanned with a CAT and Signal Generator prior to breaking ground. 2. Trial pit remained stable during excavation. 3. Groundwater not encountered. 4. Trial pit filled with flint gravel up to ground level for duration of soakaway testing. 5. Soakaway test carried out at 0.90m bgl 6. Upon completion of three soakaway tests, gravel was removed and excavation continued in order to test the extent of the underlying strata. 7. Trial pit backfilled with arising upon completion.
All dimensions in metres	
Scale: 1:25	
Method Used: Machine dug	Plant Used: JCB-3CX
Logged By: adamjones	Checked By: AGS



APPENDIX C TEST RECORDS



STRUCTURAL SOILS LTD
INSITU TESTING REPORT

Report No. 745786R.01(00)

Date 28-July-2015 Contract Green Lane, Chesterton

Client RSK Environment Ltd
Address Abbey Park
Humber Road
Coventry
CV3 4AQ

For the Attention of Michael Lawson

Order received	08-July-2015	Client Reference	None
Testing Started	20-July-2015	Client Order No.	P0250787
Testing Completed	22-July-2015	Instruction Type	Written

Test(s) undertaken (Not UKAS Accredited)

5no. Insitu soakaway tests carried out at locations specified by client.

Testing undertaken in the Laboratory

Environmental conditions (if relevant)

The results represent the ground conditions at the specified locations and depths at the time of testing.

Please Note: Remaining samples will be retained for a period of one month from today and will then be disposed of .
Test were undertaken on samples 'as received' unless otherwise stated.
Opinions and interpretations expressed in this report are outside the scope of accreditation for this laboratory.


Page 1 of 6

FULL SCALE SOAKAWAY TEST

In accordance with BRE Digest 365

Soakaway Test - Position ID : TP9


PLOT OF DEPTH OF WATER BELOW GROUND LEVEL AGAINST TIME

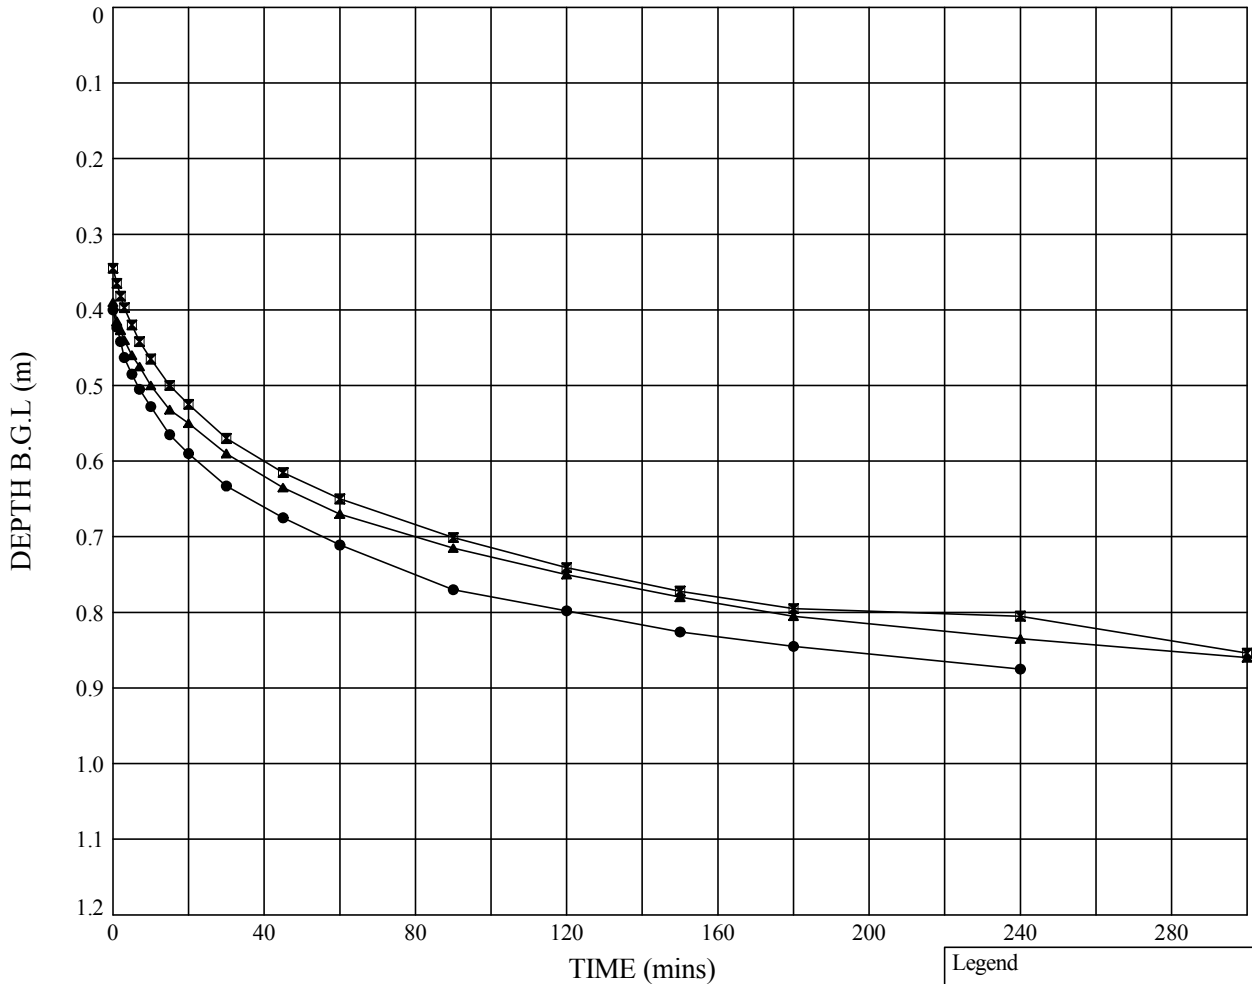


	Test 1	Test 2	Test 3	
Pit start depth:	= 1.10	1.10	1.10	m
Pit final depth:	= 1.10	1.10	1.10	m
Effective depth, D_e	= 0.70	0.76	0.71	m
Effective storage volume, V_{p75-25}	= 1.2180	1.3137	1.2354	m^3
Surface area, a_{p50}	= 6.3500	6.5755	6.3910	m^2
Time, t_{p75-25}	= 19380	51333	25538	secs
Infiltration rate, f	= 9.90×10^{-6}	3.89×10^{-6}	7.57×10^{-6}	m/s

Please note test data was extrapolated to obtain $t_{p75-tp25}$. Notes: Test 2 - Standing water in pit prior to test., Test 3 - Standing water in pit prior to test.

Legend		
●	Test 1	(20.07.15)
■	Test 2	(21.07.15)
▲	Test 3	(22.07.15)



Approved Signatories: J.BARRETT A.FROST M.STOKES S.HANDCOCK S.PHILP M.STROWGER J.MAJOR

 <p>STRUCTURAL SOILS 1a Princess Street Bedminster Bristol BS3 4AG</p>	Compiled By	Date	Checked By	Date
	<i>S. Philp</i>	23/07/15	[Redacted]	07/15
	Contract Green Lane, Chesterton		Contract Ref: 745786	


GINT_LIBRARY_V8_05_GLB LibVersion: v8_05 - Lib0004 ProjVersion: v8_05 - Core+In Situ Testing - 0003 | Graph 1 - TP SOAKAWAY - 2 - FINAL REPORT | 745786.GPJ - v8_05 | 23/07/15 - 11:14 | SP.

FULL SCALE SOAKAWAY TEST

In accordance with BRE Digest 365


Soakaway Test - Position ID : TP10

PLOT OF DEPTH OF WATER BELOW GROUND LEVEL AGAINST TIME

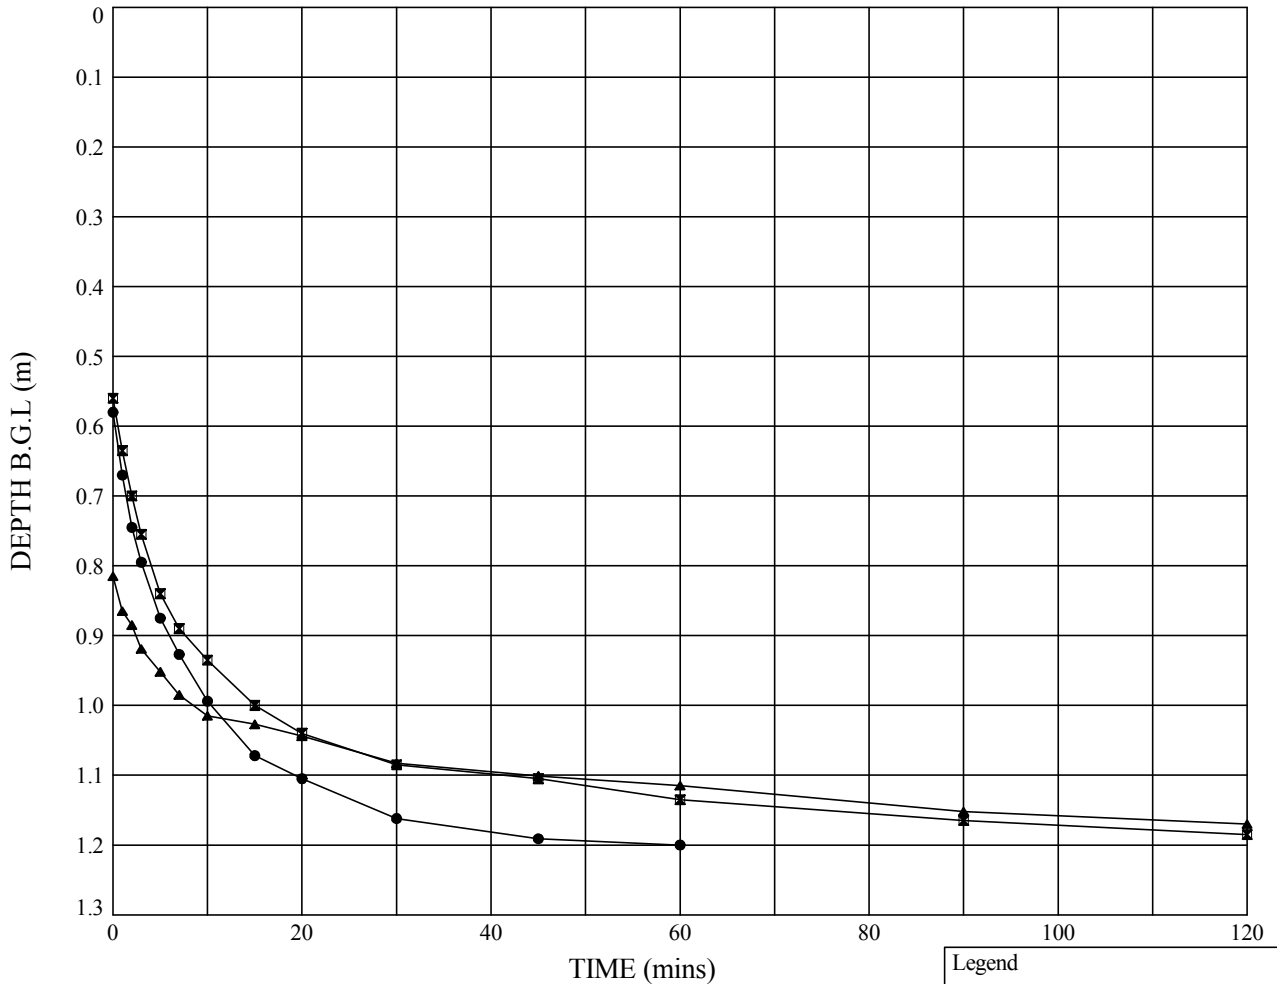


	Test 1	Test 2	Test 3	
Pit start depth:	= 1.20	1.20	1.20	m
Pit final depth:	= 1.20	1.20	1.19	m
Effective depth, D_e	= 0.62	0.64	0.37	m
Effective storage volume, V_{p75-25}	= 0.7440	0.7680	0.4440	m^3
Surface area, a_{p50}	= 4.5080	4.5760	3.6580	m^2
Time, t_{p75-25}	= 684	1058	2115	secs
Infiltration rate, f	= 2.41×10^{-4}	1.59×10^{-4}	5.74×10^{-5}	m/s

Legend		
●	Test 1	(20.07.15)
⊠	Test 2	(21.07.15)
▲	Test 3	(21.07.15)



Approved Signatories: J.BARRETT A.FROST M.STOKES S.HANDCOCK S.PHILP M.STROWGER J.MAJOR



STRUCTURAL SOILS
1a Princess Street
Bedminster
Bristol
BS3 4AG


Compiled By	Date	Checked By	Date
<i>S. Philp</i>	23/07/15	[Redacted]	□/07/1□
Contract		Contract Ref:	
Green Lane, Chesterton		745786	

FULL SCALE SOAKAWAY TEST

In accordance with BRE Digest 365

Soakaway Test - Position ID : TP11


PLOT OF DEPTH OF WATER BELOW GROUND LEVEL AGAINST TIME

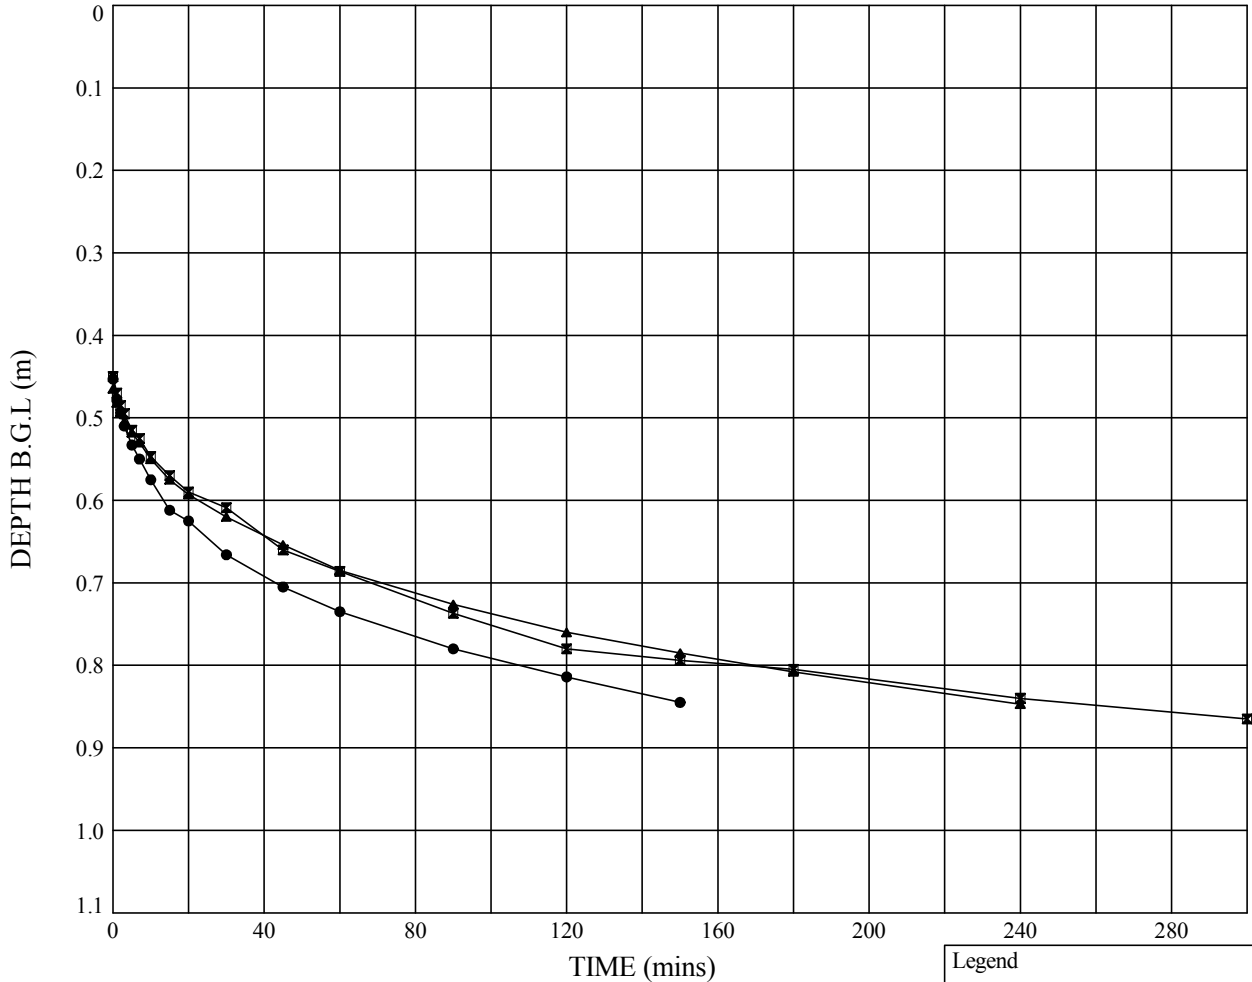


	Test 1	Test 2	Test 3	
Pit start depth:	= 1.01	1.01	0.98	m
Pit final depth:	= 1.01	0.98	0.98	m
Effective depth, D_e	= 0.56	0.53	0.51	m
Effective storage volume, V_{p75-25}	= 0.8884	0.8374	0.8135	m^3
Surface area, a_{p50}	= 5.4180	5.2900	5.2300	m^2
Time, t_{p75-25}	= 9755	13871	13254	secs
Infiltration rate, f	= 1.68×10^{-5}	1.14×10^{-5}	1.17×10^{-5}	m/s

Please note test data was extrapolated to obtain $t_{p75-tp25}$.

Legend		
●	Test 1	(20.07.15)
■	Test 2	(21.07.15)
▲	Test 3	(22.07.15)



Approved Signatories: J.BARRETT A.FROST M.STOKES S.HANDCOCK S.PHILP M.STROWGER J.MAJOR

 <p>STRUCTURAL SOILS 1a Princess Street Bedminster Bristol BS3 4AG</p>	Compiled By	Date	Checked By	Date
	<i>S. Philp</i>	23/07/15	[Redacted]	07/1
	Contract Green Lane, Chesterton		Contract Ref: 745786	


GINT_LIBRARY_V8_05_GLB LibVersion: v8_05 - Lib0004 ProjVersion: v8_05 - Core+In Situ Testing - 0003 | Graph 1 - TP SOAKAWAY - 2 - FINAL REPORT | 745786.GPJ - v8_05 | 23/07/15 - 11:16 | SP.

FULL SCALE SOAKAWAY TEST

In accordance with BRE Digest 365

Soakaway Test - Position ID : TP12

PLOT OF DEPTH OF WATER BELOW GROUND LEVEL AGAINST TIME

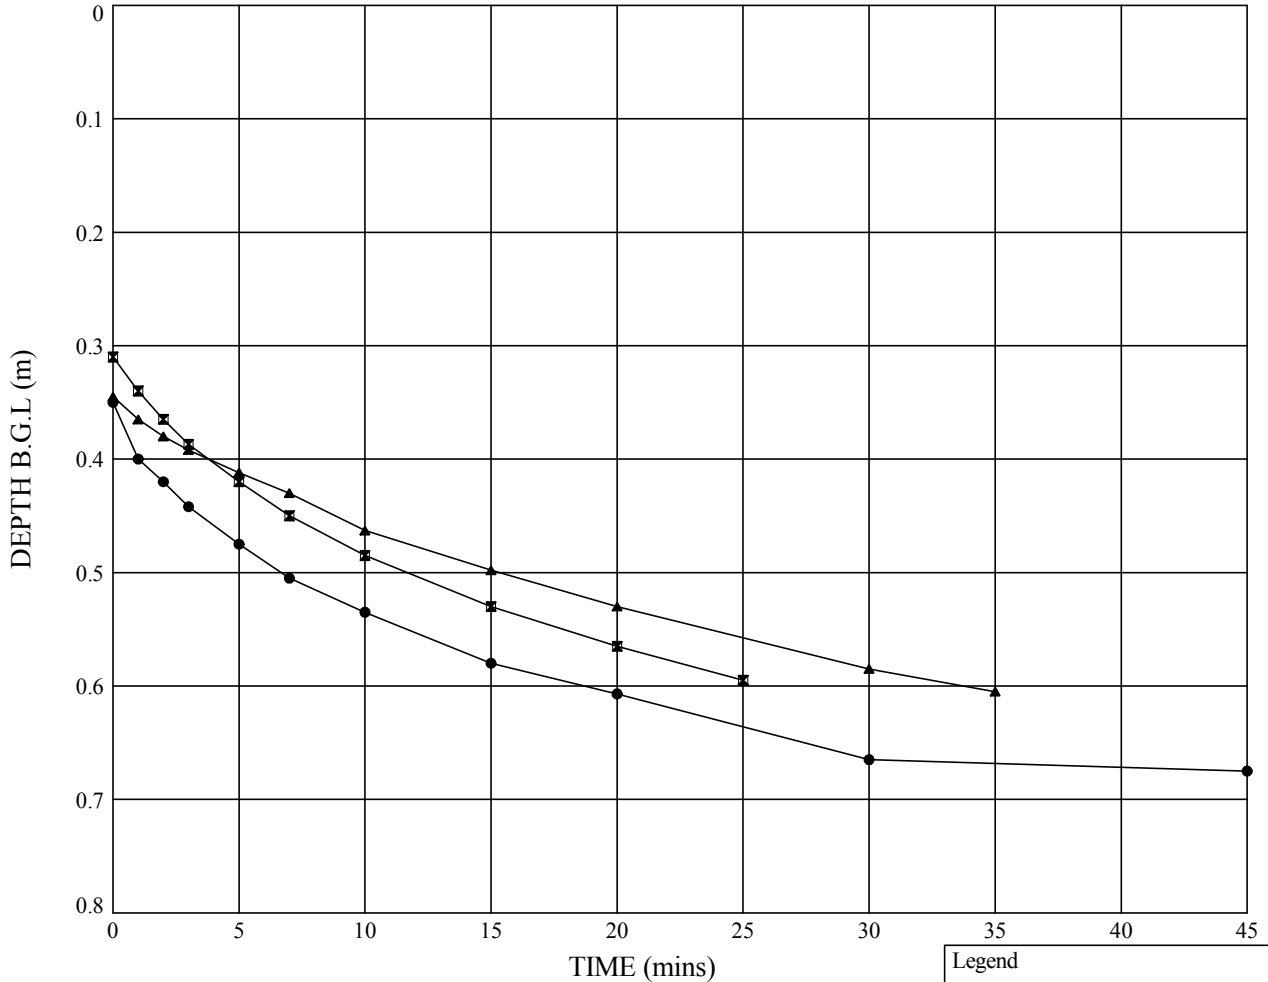

	Test 1	Test 2	Test 3	
Pit start depth:	= 0.68	0.68	0.68	m
Pit final depth:	= 0.68	0.68	0.68	m
Effective depth, D_e	= 0.33	0.37	0.33	m
Effective storage volume, V_{p75-25}	= 0.4388	0.4928	0.4455	m^3
Surface area, a_{p50}	= 3.9025	4.0505	3.9210	m^2
Time, t_{p75-25}	= 902	1156	1510	secs
Infiltration rate, f	= 1.25×10^{-4}	1.05×10^{-4}	7.52×10^{-5}	m/s

Legend

- Test 1 (20.07.15)
- Test 2 (21.07.15)
- ▲ Test 3 (21.07.15)


Plan (Not to scale)

← 2.70 →

1.00

No Bearing Taken

Approved Signatories: J.BARRETT A.FROST M.STOKES S.HANDCOCK S.PHILP M.STROWGER J.MAJOR

 <p>STRUCTURAL SOILS 1a Princess Street Bedminster Bristol BS3 4AG</p>	Compiled By	Date	Checked By	Date
	<i>S. Philp</i>		<input checked="" type="checkbox"/>	<input type="checkbox"/>
	Contract		Contract Ref:	
Green Lane, Chesterton		745786		


GINT_LIBRARY_V8_05_GLB LibVersion: v8_05 - Lib0004 ProjVersion: v8_05 - Core+In Situ Testing - 0003 | Graph 1 - TP SOAKAWAY - 2 - FINAL REPORT | 745786.GPJ - v8_05 | 23/07/15 - 11:17 | SP.

FULL SCALE SOAKAWAY TEST

In accordance with BRE Digest 365

Soakaway Test - Position ID : TP13

PLOT OF DEPTH OF WATER BELOW GROUND LEVEL AGAINST TIME

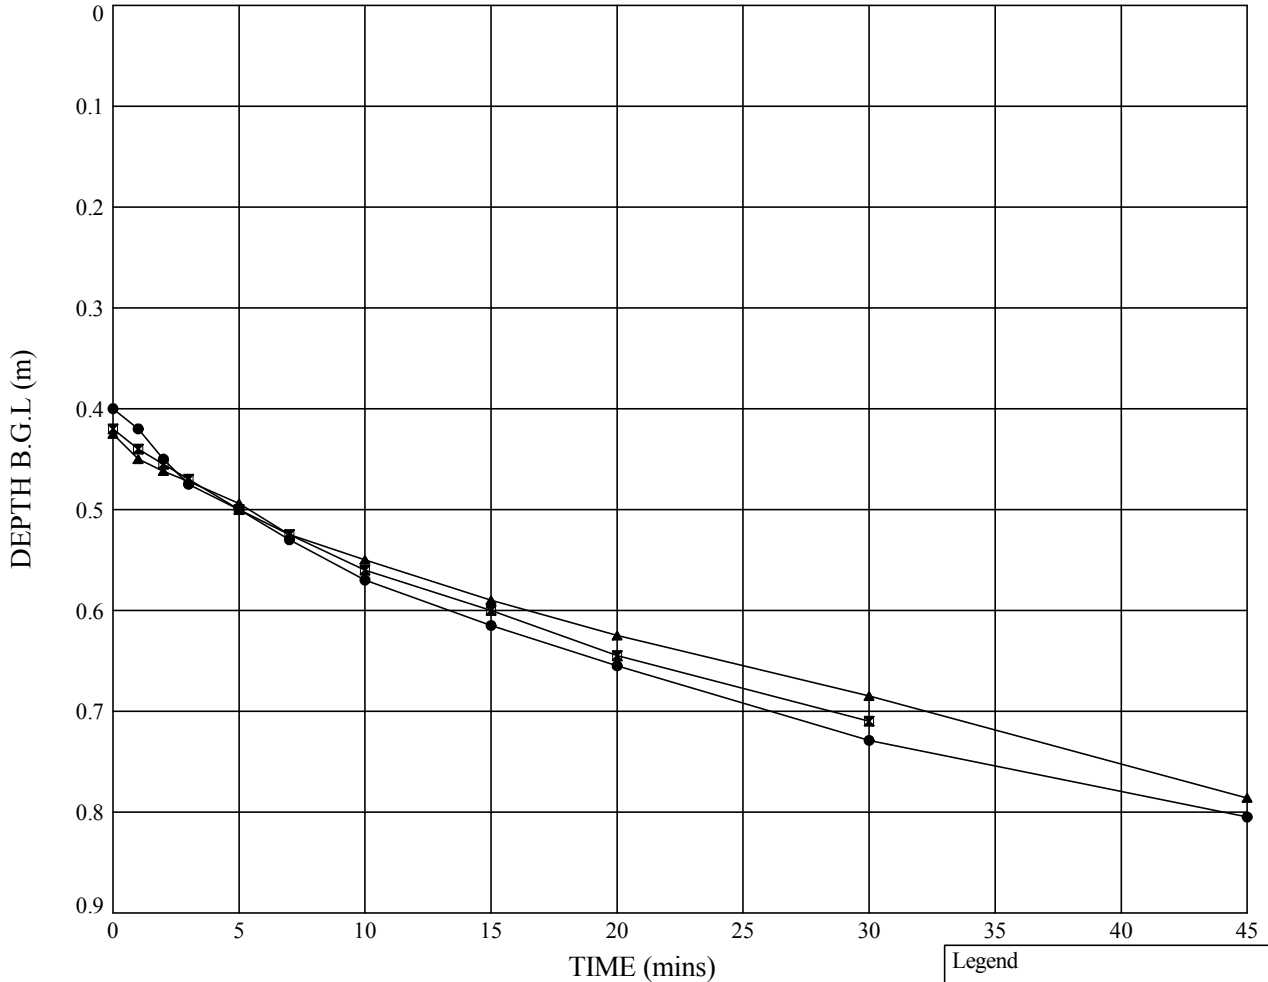

	Test 1	Test 2	Test 3	
Pit start depth:	= 0.81	0.81	0.81	m
Pit final depth:	= 0.81	0.81	0.81	m
Effective depth, D_e	= 0.41	0.39	0.38	m
Effective storage volume, V_{p75-25}	= 0.5670	0.5390	0.5320	m^3
Surface area, a_{p50}	= 4.3390	4.2630	4.2440	m^2
Time, t_{p75-25}	= 1290	1410	1622	secs
Infiltration rate, f	= 1.01×10^{-4}	8.97×10^{-5}	7.73×10^{-5}	m/s

Legend

- Test 1 (20.07.15)
- Test 2 (21.07.15)
- ▲ Test 3 (21.07.15)


Plan (Not to scale)

2.80

1.00

No Bearing Taken

Approved Signatories: J.BARRETT A.FROST M.STOKES S.HANDCOCK S.PHILP M.STROWGER J.MAJOR

 <p>STRUCTURAL SOILS 1a Princess Street Bedminster Bristol BS3 4AG</p>	Compiled By	Date	Checked By	Date
	<i>S. Philp</i>	23/07/15	[Redacted]	07/15
	Contract		Contract Ref:	
Green Lane, Chesterton		745786		

GINT_LIBRARY_V8_05_GLB LibVersion: v8_05 - Lib0004 ProjVersion: v8_05 - Core+In Situ Testing - 0003 | Graph 1 - TP SOAKAWAY - 2 - FINAL REPORT | 745786.GPJ - v8_05 | 23/07/15 - 11:19 | SP.
