

Project

Project Name: The Bungalow White Post Road Bodicote OX15 4BN Post Repair

Project Description: Post Repair CCTV Survey

Project Date: 21/11/2022





Table of Contents

Project Name	Project Number	Project Date
The Bungalow White Post Road Bodicote OX15 4BN Post Repair		21/11/2022

Project Information	P-1
Section: 1; MH02 > MH01 (MH02X)	1



Project Information

Project Name	Project Number	Project Date
The Bungalow White Post Road Bodicote OX15 4BN Post Repair		21/11/2022

Client

Company: Debbie Whitford
Department: The Bungalow
Street: White Post Road
Town or City: Bodicote
Post Code: OX15 4BN

Contractor

Company: Assured Drainage
Street: 49 Beaconsfield Road
Town or City: Banbury
County: Oxfordshire
Post Code: OX16 9EP
Phone: 07566 221 736



Project Information

Project Name	Project Number	Project Date
The Bungalow White Post Road Bodicote OX15 4BN Post Repair		21/11/2022

Project Summary

As the re-round did not fully reform the drains as required the decision was taken to excavate the worst of the deformed drain. During the excavation roots of 100mm diameter were the cause of the deformation in the drainage. Furthermore there were several roots in the region of 75mm causing deformation to the drain. On inspection of the drain off boundary to the village hall ic cover root intrusion and cracked clay pipe have been observed. The roots have been removed but the drain remains damaged. This may cause future issues.



Assured Drainage

Assured Drainage
49 Beaconsfield Road, Banbury
Tel. 07566 221 736

Project Information

Project Name	Project Number	Project Date
The Bungalow White Post Road Bodicote OX15 4BN Post Repair		21/11/2022

Project Notes


Attend site to re-round and reline drains



Section Inspection - 14/11/2022 - MH02X

Section 1	Inspection 1	Date 14/11/22	Time 16:53	Client's Job Ref DEBBIE WHITFORD	Weather No Rain Or Snow	Pre Cleaned No	PLR MH02X
Operator SHAWN		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID 1

Town or Village:	Bodicote	Inspection Direction:	Downstream	Upstream Node:	MH02
Road:	White Post Road	Inspected Length:	11.40 m	Upstream Pipe Depth:	0.410 m
Location:	Gardens	Total Length:	11.40 m	Downstream Node:	MH01
Surface Type:		Joint Length:	0.00 m	Downstream Pipe Depth:	0.730 m
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Year Constructed:		Pipe Material:	Fibreglass reinforced pipe		
Flow Control:	No flow control	Lining Type:	Cured in place lining		
Inspection Purpose:	Post completion inspection of repairs or renovations	Lining Material:	No Lining		
Comments:	GENERAL CCTV SURVEY				
Recommendations:					

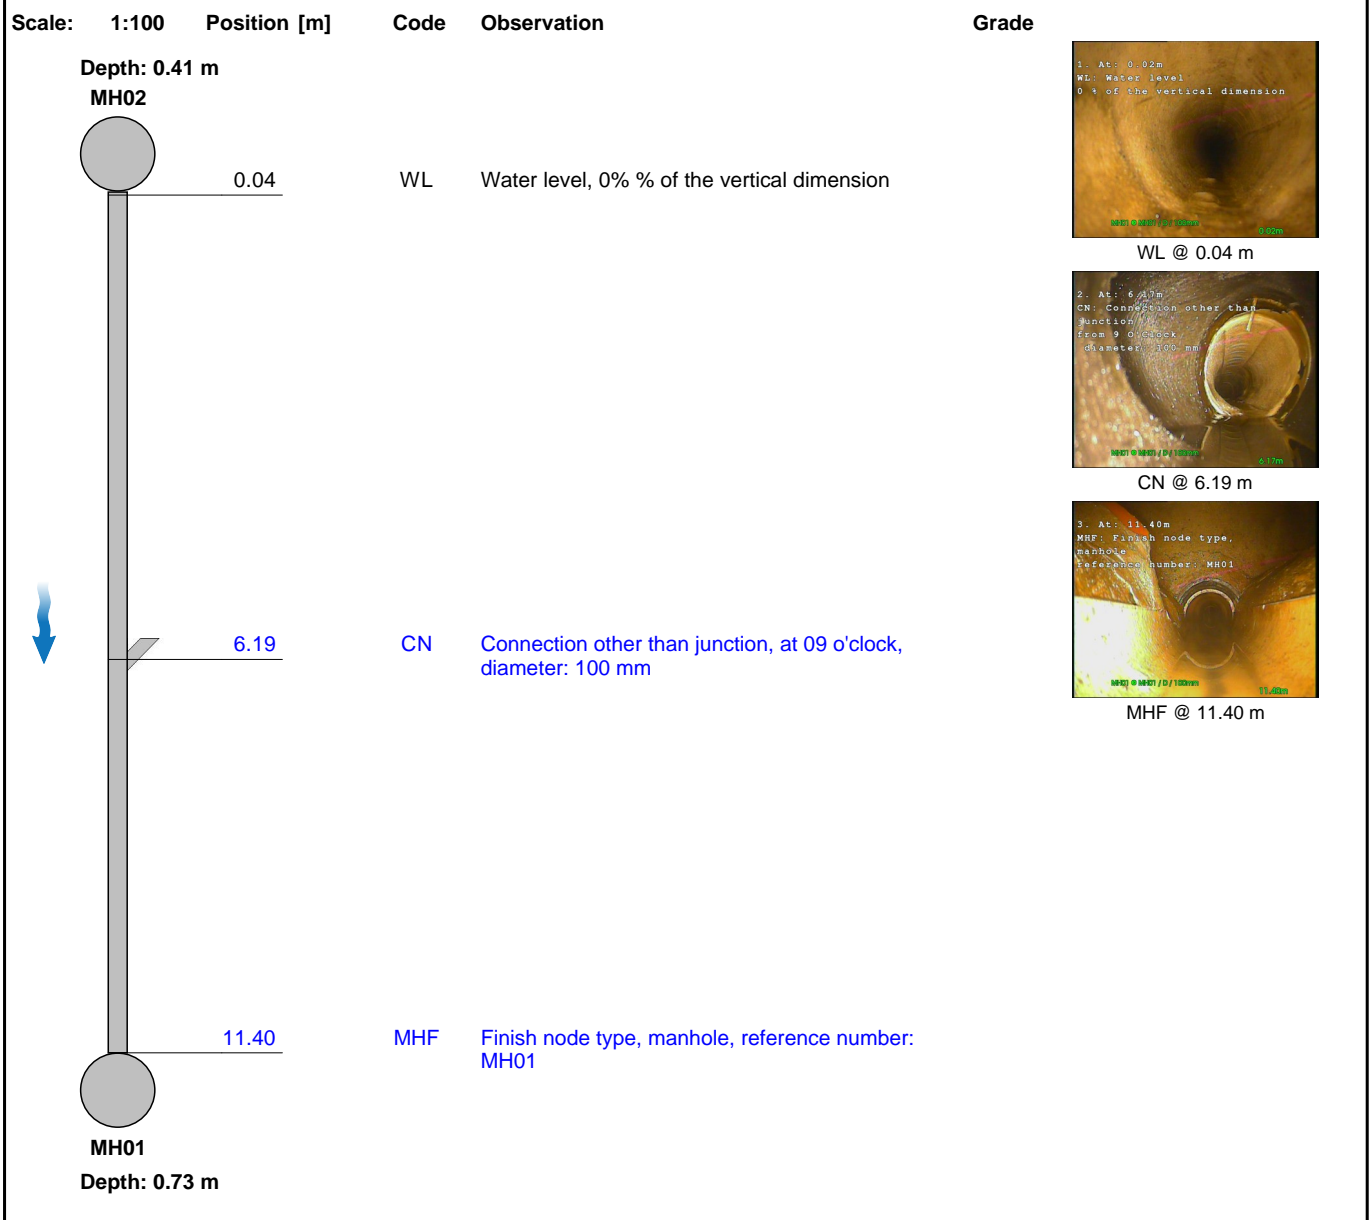

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 14/11/2022 - MH02X


Section	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
1	Downstream	MH02X	DEBBIE WHITFORD	THE BUNGALOW



221114_1652A-Survey.jpg, 00:00:00, 0.04 m
Water level, 0% of the vertical dimension



221114_1652B-Survey.jpg, 00:00:29, 6.19 m
Connection other than junction, at 09 o'clock, diameter: 100 mm

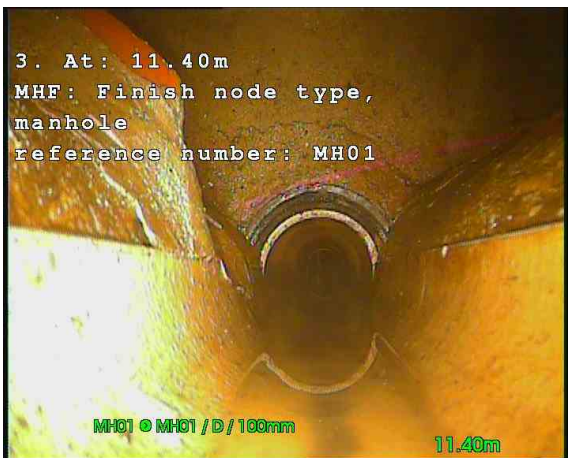

221114_1653A-Survey.jpg, 00:00:57, 11.40 m
Finish node type, manhole, reference number: MH01
